Solvay UFSD Facilities Update

January 14, 2019





\$6,400,000 Capital Project

- Middle School
 - Parking lot expansion
 - Playground improvements
 - Bleacher replacement
 - Corridor painting
 - Gym floor refinishing (original Gym)
- Project closeout: February/March 2019






- Phase 1 Middle School
 - Roof replacement, including skylight infill
- Phase 2A Existing Bus Garage
 - Demolition
- Both Phase 1 and 2A have bid and are under budget
 - Bus Garage demolition: Spring 2019
 - MS roof replacement: Summer 2019





MS Roof - Fall 2018











- Phase 2B Middle School, Storage Building, New Transportation Center
 - Door hardware replacement
 - Main entrance renovations
 - Fire alarm and temperature control upgrades
 - New Maintenance Storage Building at Solvay MS
 - New Transportation Center






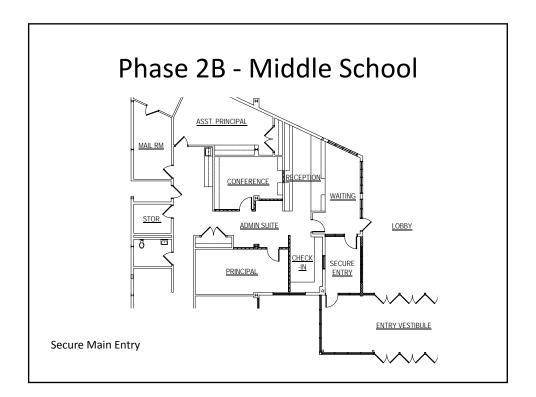

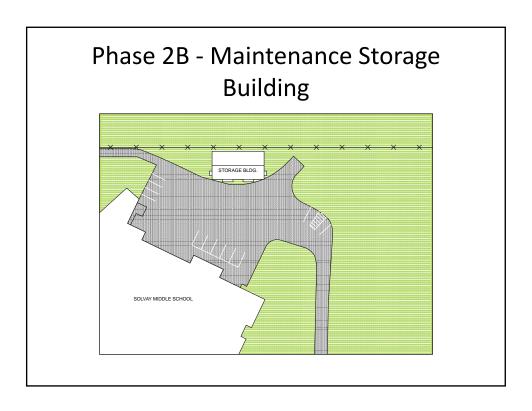



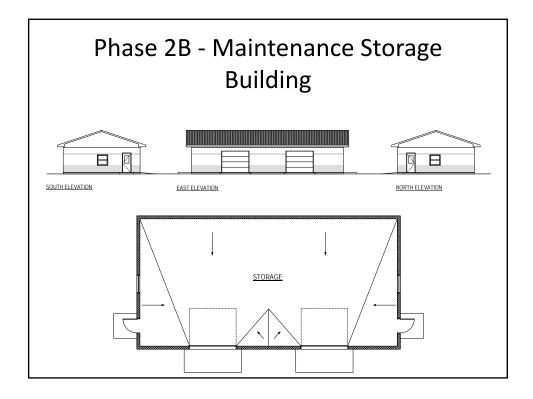

- Multiple programming meetings with Bobbie Jo Eastman (Transportation Supervisor) and Scott Pittsley (Mechanic)
- Site visits to other Transportation Centers
 - Phoenix
 - Chittenango
 - Weedsport
 - Marcellus











Chittenango CSD




Phoenix CSD



Marcellus CSD



Weedsport CSD

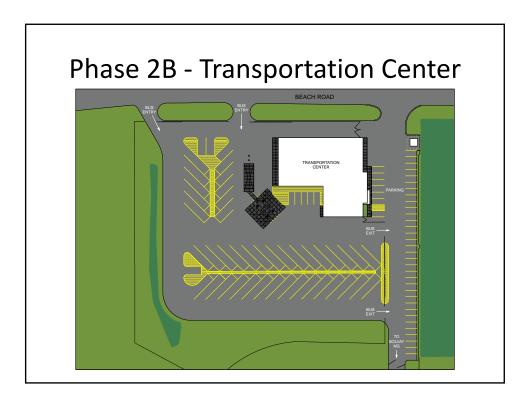





Lobby



Mail/Keys




Dispatch Office



Supervisor's Office



Training Room



Maintenance Bays



Maintenance Bays

\$28,242,000 Capital Project

- Phase 2B
 - Bid Opening: 2/4/19
 - Award of Contracts: 2/11/19
 - Construction:
 - Maintenance Storage Building: Spring/Summer 2019
 - Middle School: Summer 2019
 - Transportation Center: Spring 2019 through Spring 2020





- Phase 3 Elementary School and High School
 - ES renovations
 - Secure main entrance
 - Air conditioning
 - HS renovations
 - Secure main entrance
 - Auditorium renovations
 - Corridor improvements





\$28,242,000 Capital Project

- Phase 3 HS Auditorium:
 - Programming meetings with Auditorium Committee:
 - CJ Oliver
 - Diane Hagemann
 - Gerry Fitzgerald
 - Kermit Buckman
 - Karen Henry
 - Jay Tinklepaugh

- Kevin VanBeveren
- Kim McGraw
- Lena-Rose Orlando
- Frank Lopez
- Ty Marshall





- Phase 3 HS Auditorium:
 - Site visits with Auditorium Committee:
 - Baldwinsville HS
 - Lafayette Jr./Sr. HS
 - Homer Jr./Sr. HS
 - Homer Center for the Arts





Phase 3 – Auditorium Tours











Lafayette Jr./Sr. HS

Phase 3 – Auditorium Tours











Homer Center for the Arts

\$28,242,000 Capital Project

• Phase 3

- Bid Opening: Early 2020

- Construction: Summer/Fall 2020





2018-19 Capital Outlay Project \$100,000

- Solvay ES
 - Concrete stair replacement near bus deck (2 total)
 - Construction: Spring 2019





2020 Building Condition Survey

- Required by NYSED every five years
- Must be performed by licensed architects and/or engineers
- Focuses on future needs related to infrastructure
- Does not take into account programmatic needs





Questions?	
